


Project: msproj11  
Date: Tue 16/02/16

Task	Milestone	Project Summary	External Milestone	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	Deadline
Split	Summary	External Tasks	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	Progress

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
44		<b>Preparation for Operation in MICE hall</b>	<b>109 days?</b>	<b>Mon 15/Thu 14/07/16</b>			
45		<b>Outstanding review actions</b>	<b>1 day?</b>	<b>Mon 15/Mon 15/02/16</b>			
46		Update operating instructions	1 day?	Mon 15/Mon 15/02/16			
47		Maintenance plan for safety critical components	1 day?	Mon 15/02/16	15/02/16		
48		Compile safety file	1 day?	Mon 15/Mon 15/02/16			
49		Install hydrogen bottle pack charging station and N2 jacketed transfer line	1 day?	Mon 15/02/16	15/02/16		
50		Install vacuum rated hand-valves upstream of all vacuum gauges	1 day?	Mon 15/02/16	15/02/16		
51		Develop comprehensive emergency procedures	1 day?	Mon 15/02/16	15/02/16		
52		Define a training scheme for LH2 system operators	1 day?	Mon 15/02/16	15/02/16		
53		Implement a formal Change Request Not	1 day?	Mon 15/Mon 15/02/16			
54		Revise control system GUI	1 day?	Mon 15/Mon 15/02/16			
55		Consider minor hardware modifications in line with specific recommendations	1 day?	Mon 15/02/16	15/02/16		
56		<b>Controls and Monitoring</b>	<b>13 days?</b>	<b>Mon 15/Wed 02/03/16</b>			
57		Door on cabinet and upgrade keys	1 day?	Mon 29/Mon 29/02/16			PW
58		Remove non-H2 system wiring from H2 system ducting	1 day?	Mon 15/02/16	15/02/16		
59		Level sensors operational	1 day?	Tue 01/Tue 01/03/16			PW
60		Update program sequences	10 days	Mon 15/Fri 26/02/16			PW
61		Commission compressor control	2 days	Mon 15/Tue 16/02/16			
62		Replace faulty sensor in gas detection panel	1 day?	Wed 02/Wed 02/03/16			PW
63		<b>Miscellaneous</b>	<b>1 day?</b>	<b>Mon 15/Mon 15/02/16</b>			
64		Train system operators	1 day?	Mon 15/Mon 15/02/16			
65		Reinstall FC#2 in MICE hall	5 days	Wed 08/Tue 14/06/16	43		
66		Leak test	2 days	Wed 15/Thu 16/06/16	65		
67		Actions to be completed with installed systems	1 day	Fri 17/Fri 17/06/16	66		
68		Cooldown test with Helium	5 days	Mon 20/Fri 24/06/16	67		
69		Inspection by ISIS	3 days	Mon 27/06/16	Wed 29/06/16	68	
70		Implement changes as requested by ISIS safety inspection	10 days	Thu 30/06/16	Wed 13/07/16	69	
71		Final ISIS inspection	1 day	Thu 14/Thu 14/07/16	70		
72		Start Hydrogen cooldown	0.5 days	Fri 15/07/Fri 15/07/16	44		
73		Hydrogen absorber ready	1 day?	Fri 22/07/Mon 25/07/16	72FS+5 days		

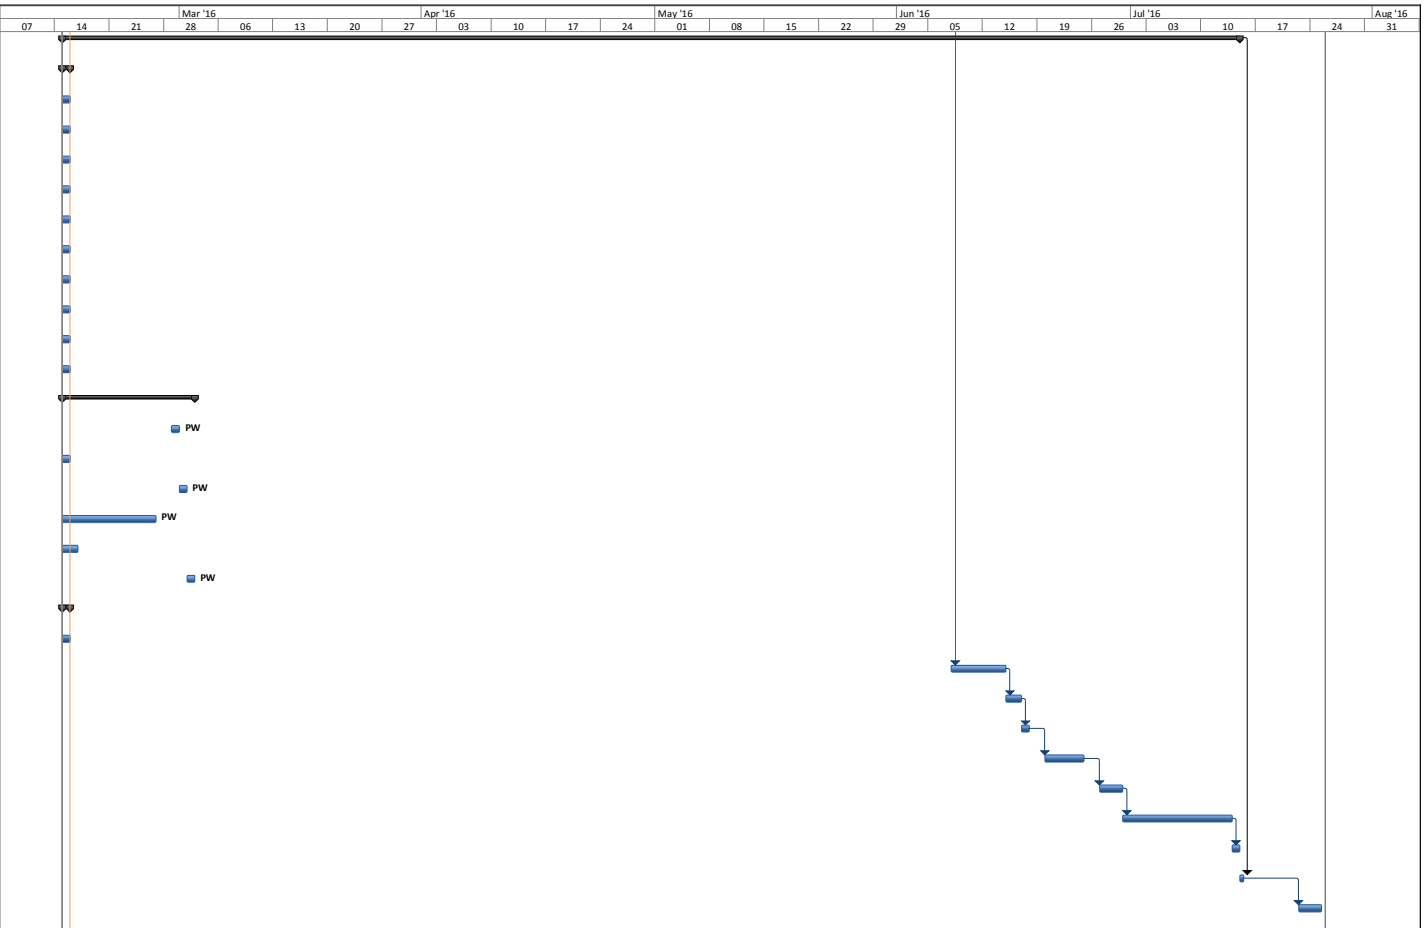

Project: msproj11  
Date: Tue 16/02/16

Task	Milestone	Project Summary	External Milestone	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	Deadline	Progress
Split	Summary	External Tasks	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	Progress	Progress
